



Builder	DRB Group
Region	North Carolina
Division	Raleigh
Community	The Farm at Neill's Creek (NC)(RAL)
Lot	00.0019
Street Address	192 Peach Grove Way
Field Manager	Brad McLoud
	Eric Morphy
Reviewer	Diana Vedock
Date	6/18/2026
Type	New Review
Product Type	Detached

Score	92.80%
Second Look, Paint & Drywall?	No
Possible Points	125.00
Adj. Possible Points	125.00
Tic Marks	9
# of Items	32
Customer Exceptions	0
Weather Exceptions	0
Division Exceptions	0
Builder Items	0
No Action Items	0

Reschedules

Tic Mark Items

Item	Tic Marks	Description	Points
Minor Drywall	3		0.25
Minor Paint	5		0.5
Minor Clean	1		0.25

Items

Room	Trade	Item	Description	Points	Initials	
Attic	Cleaning	1910 - Construction Items Left Behind	platform in attic not clean- conduit on platform	0.25		
Attic	Stairs_and_Rails	21000 - Miscellaneous	pull down stairs not cut to eliminate gap between rails at second hinge set	0.25		
Bath - 1st Floor Full	Cabinets	1630 - Drawer/Door Issue	at vanity, cabinet doors don't align with each other- right comes out past left	0.25		
Bath - 1st Floor Full	Cleaning	1920 - Trash and Debris	debris in tub drain	0.25		
Bath - 1st Floor Full	Plumbing	701 - Fixture Improperly Installed (ex: not square)	tub faucet is installed crooked	0.25		
Bath - Hall	Plumbing	700D - Damage	tub has rust staining	0.25		
Bath - Owner's	Bath_Accessories	18060 - Shower Enclosure Not Operating Properly	enclosure door, at handle, gasket not cut/ trimmed	0.25		
Bath - Owner's	Cabinets	1600D - Damage	at rightmost vanity, bottom of cabinet is damaged/ gauged	0.25		
Bath - Owner's	Ceramic	1220 - Tile Installation Issue	at half wall, schluter not alined at interior corner above seat	0.25		
Bath - Owner's	Counter_Tops	40040 - Out of Level/Square	counter overhang not consistent at vanity from left to right- over 1/4	0.25		
Bath - Owner's	Framing	1020 - Out of Plumb	shower half wall is not square/ plumb left to right and top to bottom- noteable at tile install, floor install, and shower wall install	0.25		
Bedroom - 1st Floor	Framing	1050 - Bowed Wall	right wall, approaching window, bowed/ wavy approaching corner	0.25		
Bedroom - Owner's	Windows	13010 - Difficult to Open	letmost window is difficult to open/ close- especially compared to right window in bedroom	0.25		
Bedroom 2	Electric	810 - Crooked Outlet/Switch	front right bedroom, switch plate not square/ level with corner	0.25		
Bedroom 3	Doors	50010 - Hinge Screw/Pin Issues	back left bedroom closet, top hinge is scratched/ damaged	0.25		
Exterior	Concrete_Flatwork	500 - Miscellaneous	at front, sidewalk insert in driveway has concrete overpour onto driveway both, bottom panels and apron	0.25		
Exterior	Roofing	2000D - Damage	at front left dormer, raised shigles at right overhang	0.25		
Exterior	Siding	4040 - Drip Edge	at front right gable, drip edge not aligned at joints with visible house sheathing beneath- three locations	0.25		
Exterior	Siding	4040 - Drip Edge	at right of home, front rake, drip edge is bowed in two locations	0.25		
Exterior	Siding	4030 - Soffit/Fascia Issues	at right of home, rear rake, fascia is bowed out midrun	0.25		
Foyer	Framing	1050 - Bowed Wall	behind front door entry, the wall bows out from corner to base stop	0.25		
Foyer	Framing	1050 - Bowed Wall	at transition wall from bathroom to dining room, wall bows in at center	0.25		
Garage	Concrete_Flatwork	520 - Stain	top panel of garage, closest to entry to home, staining from plumbing glue and sealants	0.25		
Kitchen/Dinette	Counter_Tops	40040 - Out of Level/Square	counter/ splashblock over dishwasher, starting at sink and headed to slider, counter is not	0.25		

			plumb/ square with wall- gap grows			
Kitchen/Dinette	Counter_Tops	40000D - Damage	island countertop is damaged closer to right side- dishwasher- side of island, under pendant prewire	0.25		
Kitchen/Dinette	Doors	50000D - Damage	pantry hardware on left door is damaged	0.25		
Kitchen/Dinette	Plumbing	700D - Damage	kitchen sink has damaged/ scuffing	0.25		
Kitchen/Dinette	Plumbing	701 - Fixture Improperly Installed (ex: not square)	fridge trim and box not installed square to baseboard	0.25		
Laundry Room	Plumbing	707 - Laundry Supply Box or Shutoff Access Issues	laundry box/ trim not level	0.25		
Loft	Drywall	1410 - Major Drywal Issue	drywall 45 degree wall return is bowed at ceiling juncture	0.25		
Stairs/Hall	Interior_Trim	1560 - Out of plumb/square	left of stainwell, approaching the coat closet, trim not square to flooring	0.25		
Stairs/Hall	Interior_Trim	1560 - Out of plumb/square	outside of first floor bedroom, closet casing not square with wall corner- reveal not consistent top to bottom	0.25		


Scored Photos



Attic
1910 - Construction Items Left Behind
platform in attic not clean- conduit on platform



Attic
21000 - Miscellaneous
pull down stairs not cut to eliminate gap between rails at second hinge set

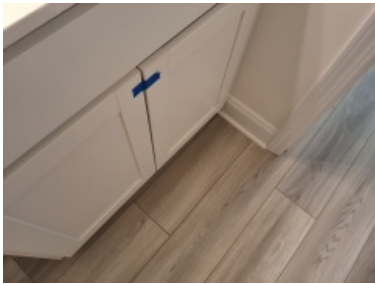

Bath - 1st Floor Full
1630 - Drawer/Door Issue
at vanity, cabinet doors don't align with each other- right comes out past left




Bath - 1st Floor Full
1920 - Trash and Debris
debris in tub drain



Bath - 1st Floor Full
701 - Fixture Improperly Installed (ex: not square)
tub faucet is installed crooked



Bath - Hall
700D - Damage
tub has rust staining

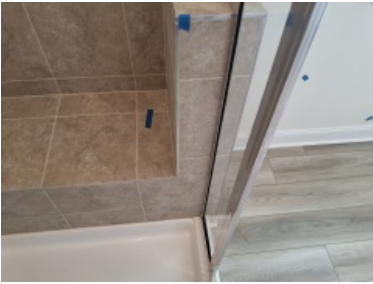

Bath - Owner's
1020 - Out of Plumb
shower half wall is not square/ plumb left to right and top to bottom- noteable at tile install, floor install, and shower wall install



Bath - Owner's
1220 - Tile Installation Issue
at half wall, schluter not alined at interior corner above seat




Bath - Owner's
1600D - Damage
at rightmost vanity, bottom of cabinet is damaged/ gauged



Bath - Owner's
18060 - Shower Enclosure Not Operating Properly
enclosure door, at handle, gasket not cut/ trimmed




Bath - Owner's
40040 - Out of Level/Square
counter overhang not consistent at vanity from left to right- over 1/4

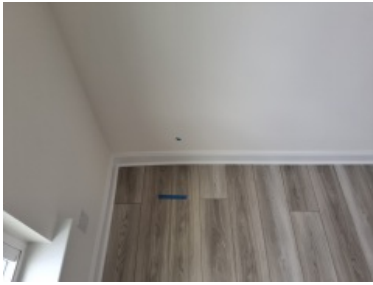

Bedroom - 1st Floor
1050 - Bowed Wall
right wall, approaching window, bowed/ wavy
approaching corner



Bedroom - Owner's
13010 - Difficult to Open
leftmost window is difficult to open/ close- especially
compared to right window in bedroom

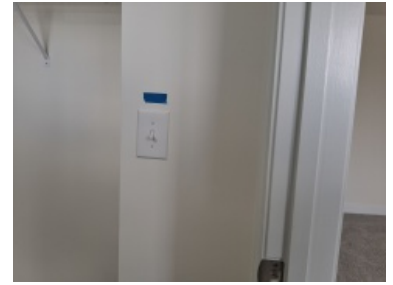

Bedroom 2
810 - Crooked Outlet/Switch
front right bedroom, switch plate not square/ level with
corner



Bedroom 3
50010 - Hinge Screw/Pin Issues
back left bedroom closet, top hinge is scratched/
damaged



Exterior
2000D - Damage
at front left dormer, raised shingles at right overhang



Exterior
4030 - Soffit/Fascia Issues
at right of home, rear rake, fascia is bowed out midrun



Exterior
4040 - Drip Edge
at front right gable, drip edge not aligned at joints with
visible house sheathing beneath- three locations



Exterior
4040 - Drip Edge
at right of home, front rake, drip edge is bowed in two
locations



Exterior
500 - Miscellaneous
at front, sidewalk insert in driveway has concrete overpour
onto driveway both, bottom panels and apron



Foyer
1050 - Bowed Wall
at transition wall from bathroom to dining room, wall
bows in at center



Foyer
1050 - Bowed Wall
behind front door entry, the wall bows out from corner to
base stop




Garage
520 - Stain
top panel of garage, closest to entry to home, staining from plumbing glue and sealants



Kitchen/Dinette
40000D - Damage
island countertop is damaged closer to right side- dishwasher- side of island, under pendant prewire



Kitchen/Dinette
40040 - Out of Level/Square
counter/ splashblock over dishwasher, starting at sink and headed to slider, counter is not plumb/ square with wall- gap grows

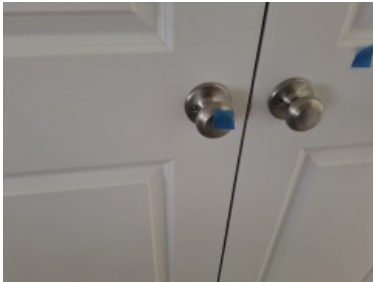

Kitchen/Dinette
50000D - Damage
pantry hardware on left door is damaged




Kitchen/Dinette
700D - Damage
kitchen sink has damaged/ scuffing




Kitchen/Dinette
701 - Fixture Improperly Installed (ex: not square)
fridge trim and box not installed square to baseboard




Laundry Room
707 - Laundry Supply Box or Shutoff Access Issues
laundry box/ trim not level

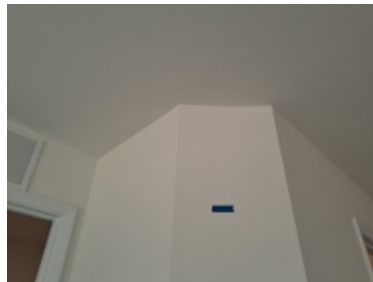

Loft
1410 - Major Drywal Issue
drywall 45 degree wall return is bowed at ceiling juncture

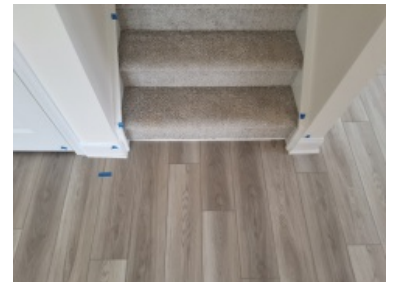

Stairs/Hall
1560 - Out of plumb/square
left of stairwell, approaching the coat closet, trim not square to flooring

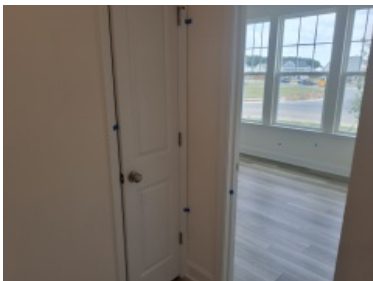

Stairs/Hall
1560 - Out of plumb/square
outside of first floor bedroom, closet casing not square with wall corner- reveal not consistent top to bottom



